



The Historic



# Dunbar Theatre

Concrete Replacement Project

Sutherland Builders, Inc.

April 2020



A Power CDC Project

**Photo Compilation**  
**April 2020**





# April 6, 2020


- Day 1
- Prep work for jackhammering of footings
- Movement of sand





# April 7, 2020

- Day 2
- Continued Prep Work
- Sectioning of areas for future concrete pouring

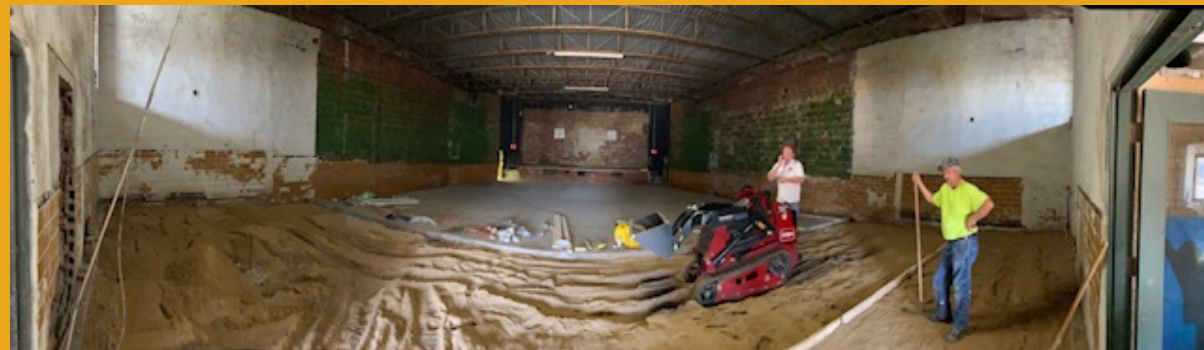



# April 8, 2020

- Day 3
- Sand placement completed
- Rebar wire screening is staged and ready





# April 9, 2020

- Day 4
- Final sand placement and prep work
- Rebar and wire screening is staged and ready






# April 10, 2020



- Day 5
- Rebar, Plastic Sheeting, and Wire Mesh in place
- City Inspection completed!





# April 13, 2020




- Day 6
- Pouring of concrete in the west section!
- Prepping for tomorrow's second pour





# April 14, 2020

- Day 7
- Completed pouring of east section of floor
- Beginning clean up

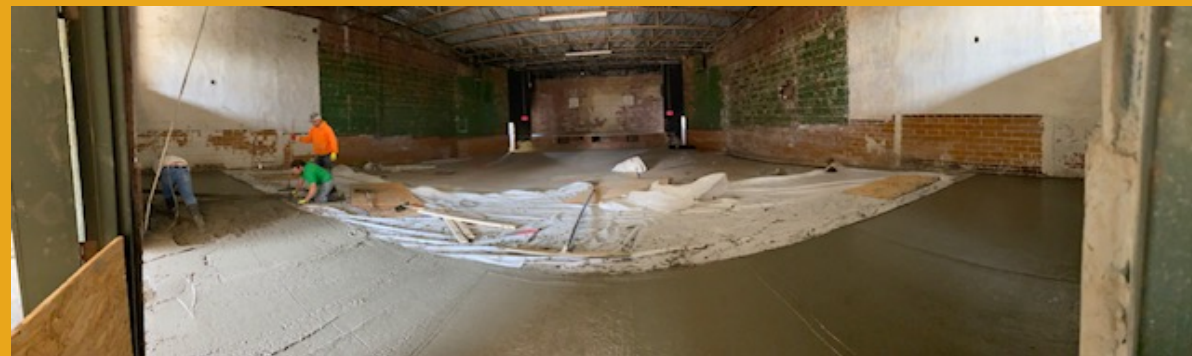





# April 15, 2020



- Day 8
- Major clean-up completed!
- Curing





# April 22, 2020

- Day 9
- Inspection and Review of Work!
- Ready to go!



Stay Abreast of our Progress!



[www.historicdunbartheatre.com](http://www.historicdunbartheatre.com)

@DunbarWichita



Friends of the Historic Dunbar Theatre  
(@HistoricDunbarTheatre)



# Help Rehabilitate the Historic Dunbar Theatre!



\$100

Support the  
\$1<sup>00</sup>  
a week campaign!

\$1.00 per week will help provide operating funds to support the rehabilitation and construction activities!

SET UP YOUR WEEKLY \$1.00 DONATION AT  
[WWW.HISTORICDUNBARTHEATRE.COM/](http://WWW.HISTORICDUNBARTHEATRE.COM/)

YOUR DONATION IS TAX DEDUCTIBLE TO THE EXTENT ALLOWED BY LAW.



# Thank You!



**One-time, and ongoing, support is necessary to return the Historic Dunbar Theatre to prominence in the community, serve as a catalyst for growth, and a harbinger for development in the Dunbar District of the McAdams Neighborhood.**
